



# **MOZAMBIQUE UPDATE ON DEMINING COMPLETION**

Meeting of the MASG  
New York, 18 October 2013

By Hans Risser and Justus Okoko



## Background

- Mozambique landmine problem was once one of the most severe in the world, with a legacy of landmines and explosive remnants of war from decades of conflict.
- Clearance of all mined areas seemed like a distant prospect, but its becoming clear that in 2014 Mozambique will be in the final stages of clearing all known mined areas in the country.
- Mozambique is seen as a symbol of what can be achieved under the Mine Ban Convention given strong government leadership, political will to complete the job and sufficient international support and assistance.




## Landmine Use in Mozambique

- Landmines were widely used by all sides in the independence struggle and wars of destabilization that ended in 1992.
- Almost no maps were maintained of where landmines were placed resulting in large, undefined suspected areas with small numbers of scattered mines.
- A Landmine Impact Survey (LIS) completed in August 2001 found landmines located in all 10 provinces of Mozambique and 123 of its 128 districts, subsequently affecting over 1.4 million people in 791 communities.



## Demining in Mozambique

- 1993-2007 focused on high-priority humanitarian areas resulting in reduced casualty figures.

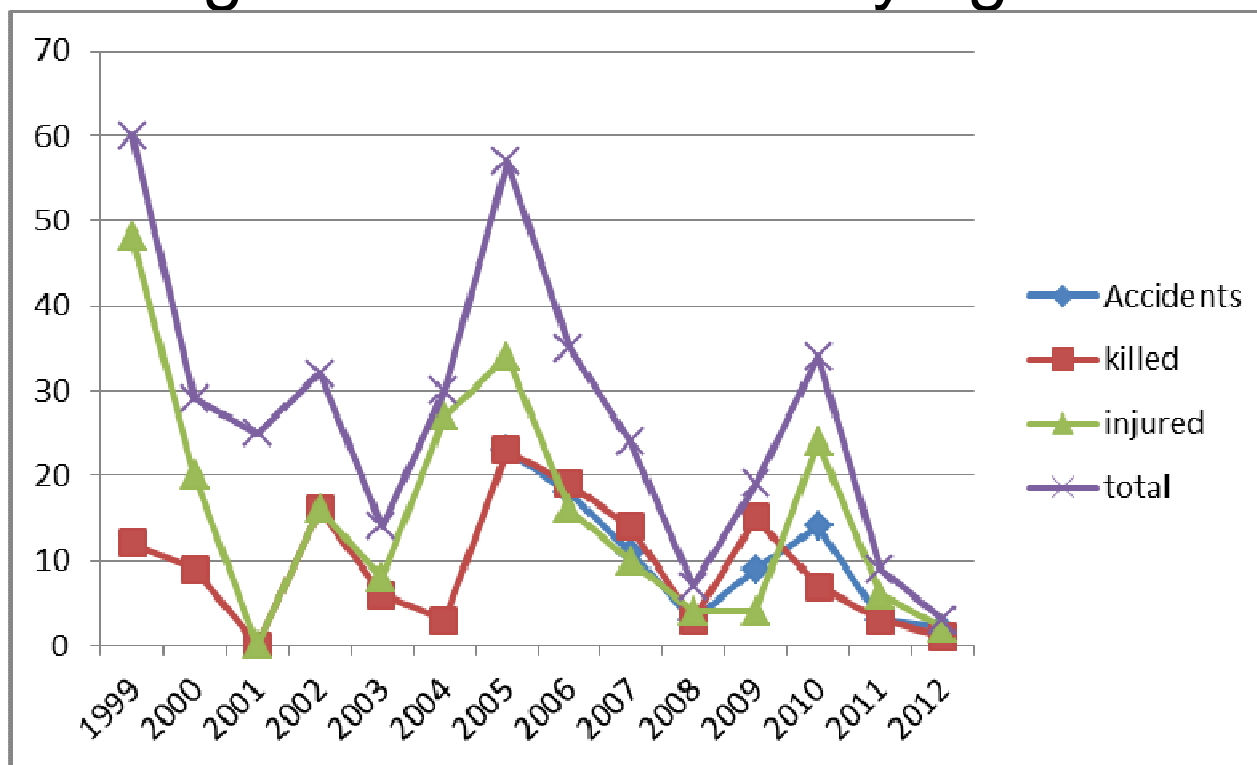



## Summary of progress achieved, 2009 -2013


### Planned implementation results versus actual demining results 2008-2012

Year	Planned Results		Actual Results			
	Number of areas	Amount of area m2	Number of areas	Amount of area m2	Mines destroyed	UXO destroyed
2008	203	1,571,252	237	2,346,130	1142	846
2009	82	1,997,266	126	4,314,197	914	871
2010	100	2,239,402	136	6,134,630	883	531
2011	28	2,574,329	229	7,204,777	8487	406
2012	104	2,503,476	255	8,714,708	9053	1126
<b>Total</b>	<b>517</b>	<b>10,885,725</b>	<b>983</b>	<b>28,714,442</b>	<b>20,479</b>	<b>3,780</b>



## Suspected Hazard Area Released from 2008 until 2012 compared to original plan

**Mozambique has achieved more than originally planned during the last 5 years thanks to the better coordination by the Government and continuing support from more than 20 international partners.**

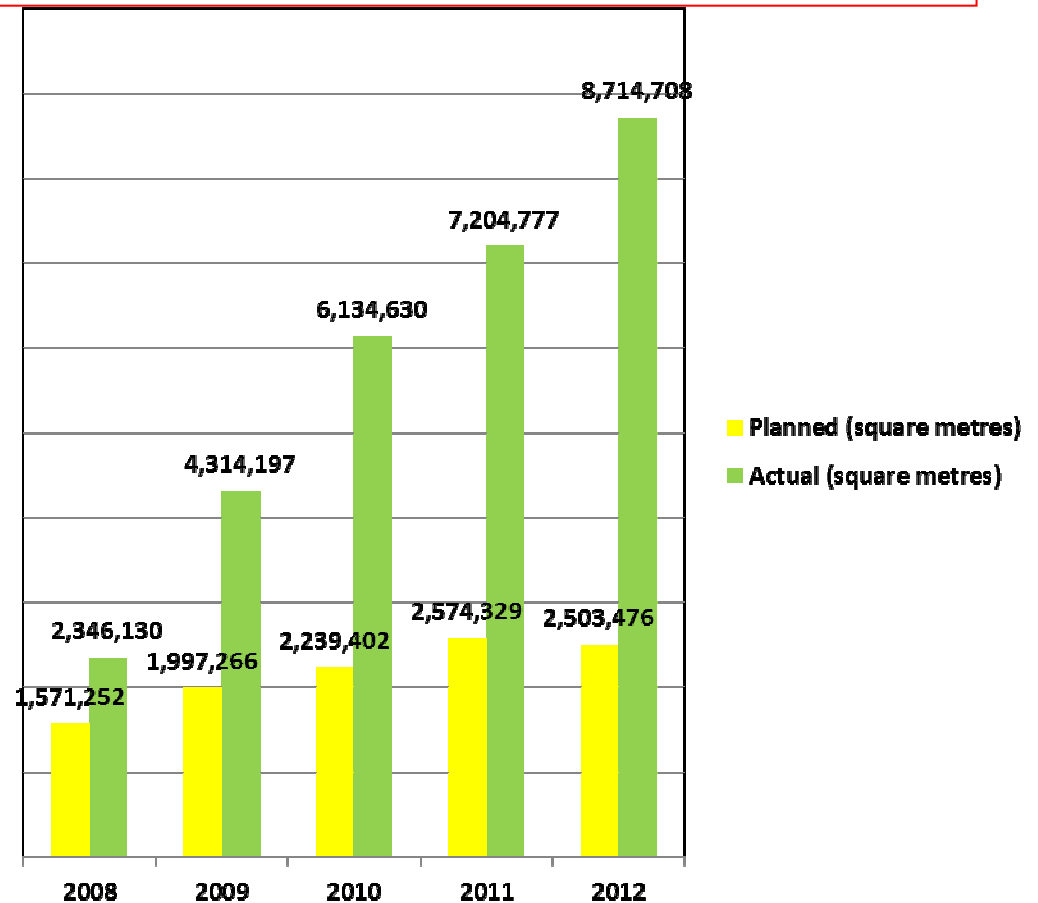




## Summary of progress achieved, 2009 -2013

### Additional surveys required to clarify the remaining mined area:


- District-by-District Approach provides clear monitoring of progress.
- Utilizing the district-by-district approach, able to declare 101 districts out of a total of 128 districts as 'mine-free', meaning there are no known mined areas remaining in these districts.
- 5 Provinces (Gaza, Cabo Delgado, Nampula, Niassa and Zambezia) out of the 10 provinces in the country are now free of all known mined areas.




## MINE AFFECTED DISTRICTS IN 2008, 2010, 2013

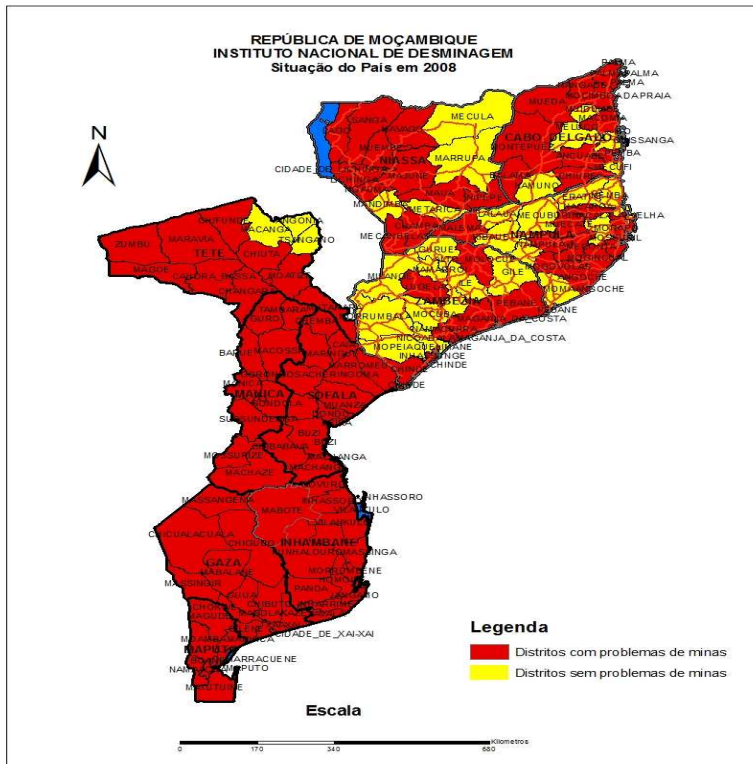

2008

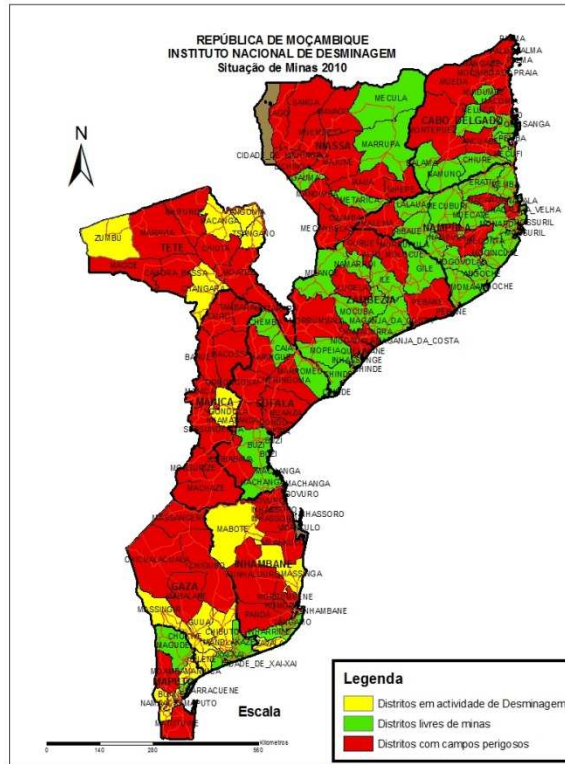

2010

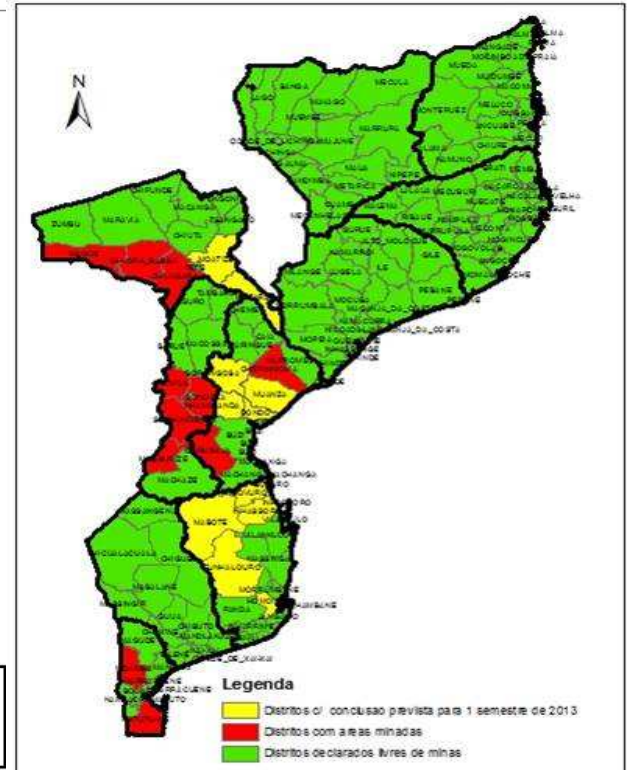

2013





## Remaining Mine Suspected Areas as of 31.08.2013

PROVINCE	Districts	Baseline Tasks		Non-Baseline Tasks		Total	
		Areas	m2	Areas	m2	Areas	m2
MAPUTO	3	-	-	12	499,961	12	499,961
INHAMBANE	6	29	172,630	16	334,976	45	507,606
SOFALA	8	32	629,553	102	3,867,866	134	4,497,419
MANICA	4	2	303,784	17	1,581,349	19	1,885,133
TETE	4	-	-	11	876,722	11	876,722
<b>Total</b>	<b>25</b>	<b>63</b>	<b>1,105,967</b>	<b>158</b>	<b>7,160,874</b>	<b>221</b>	<b>8,266,841</b>



## Mine Action Work Plan For 2014

Province	District	Tasks	Description	Area (m2)	Remarks
<b>Sofala</b>	Cheringoma	3	Road Tasks Requiring Mechanical Demining	622,000	Delayed demining in 2013 due to late arrival of demining machine
<b>Sofala</b>	Chibabava	75	Mine suspected areas	1,571,030	Delayed demining in 2013 due to access and insecurity
<b>Sofala</b>	Nhamatanda	1 (62 Towers)	Beira I & II Powerlines	155,000	Delayed demining in 2013 due to difficult road access
<b>Manica</b>	Gondola	1 (15 Towers)	Beira I & II Powerlines	33,000	Delayed demining in 2013 due to lack of mechanical demining assets
<b>Manica</b>	Manica	3	Nhamucuarara, Mucudo, Mudododo border minefields	453,300	Border minefields with access from Zimbabwe
<b>Manica</b>	Mossurize	14	Mine Suspected areas	545,652	New Surveys identified areas in 2013, close to border
<b>Tete</b>	Cahora Bassa	1	Chinzunga section of Cahora Bassa Mine Belt	75,000	Delayed demining in 2013 due to difficult road access
<b>Tete</b>	Cahora Bassa	1	Kahira Luia Border Minefield	344,970	Border minefield with access from Zimbabwe
<b>Tete</b>	Magoe	1	N'soluwamuthu Border Minefield	220.000	Border minefield with access from Mozambique
<b>Total</b>		100 Tasks		4.019.952	



## Demining Completion in 2014

- To complete demining in 2014, the National Demining Institute estimates a total budget of about 13million USD will be required in 2014.

<b>Total estimated amount</b>	<b>13.284.856 USD</b>
Government contribution	2.000.000 USD
International contribution pledged	3.000.000 USD
Unfunded	8.284.856 USD

- Demining in 2014 will need to:
  - overcome technical challenges encountered along the powerlines and border minefields,
  - ensure bilateral cooperation with Zimbabwe on border minefields; and
  - maintain security in central region.



## Preparations and support to the 3RC

- Government of Mozambique is committed to making necessary preparations for the 3<sup>rd</sup> Review Conference. As depositor of the Convention, the UNSG will formally request Mozambique to convene the 3<sup>rd</sup> Review Conference.
- UN will provide support to the organization of the Review Conference through the UN Office of Disarmament Affairs and UNDP.

Total Estimated Cost to Organize the 3RC	\$1,010,180 USD
Government of Mozambique contribution	\$200,000 USD
<b>Amount Requested from International Partners</b>	<b>\$810,180 USD</b>



## Expected Level of Participation

- 800-1000 delegates are expected to attend the Maputo Review Conference, including representatives of :
  - 160 States Parties
  - Observer States
  - UN Agencies and International Organizations.
  - NGOs
  - Civil Society Representatives
- States Parties will be invited to attend at Ministerial Level.



## Conclusion

- The monumental progress achieved in demining Mozambique only possible through the Government's leadership and continuing support of International Community.
- The Review Conference is a chance to support and celebrate Mozambique success in demining and mine action globally.
- Government of Mozambique is preparing to organize briefings on preparations for the 2014 Review Conference and request additional support from International Partners to complete demining and host the Review Conference.



New York, 18 October 2013
